


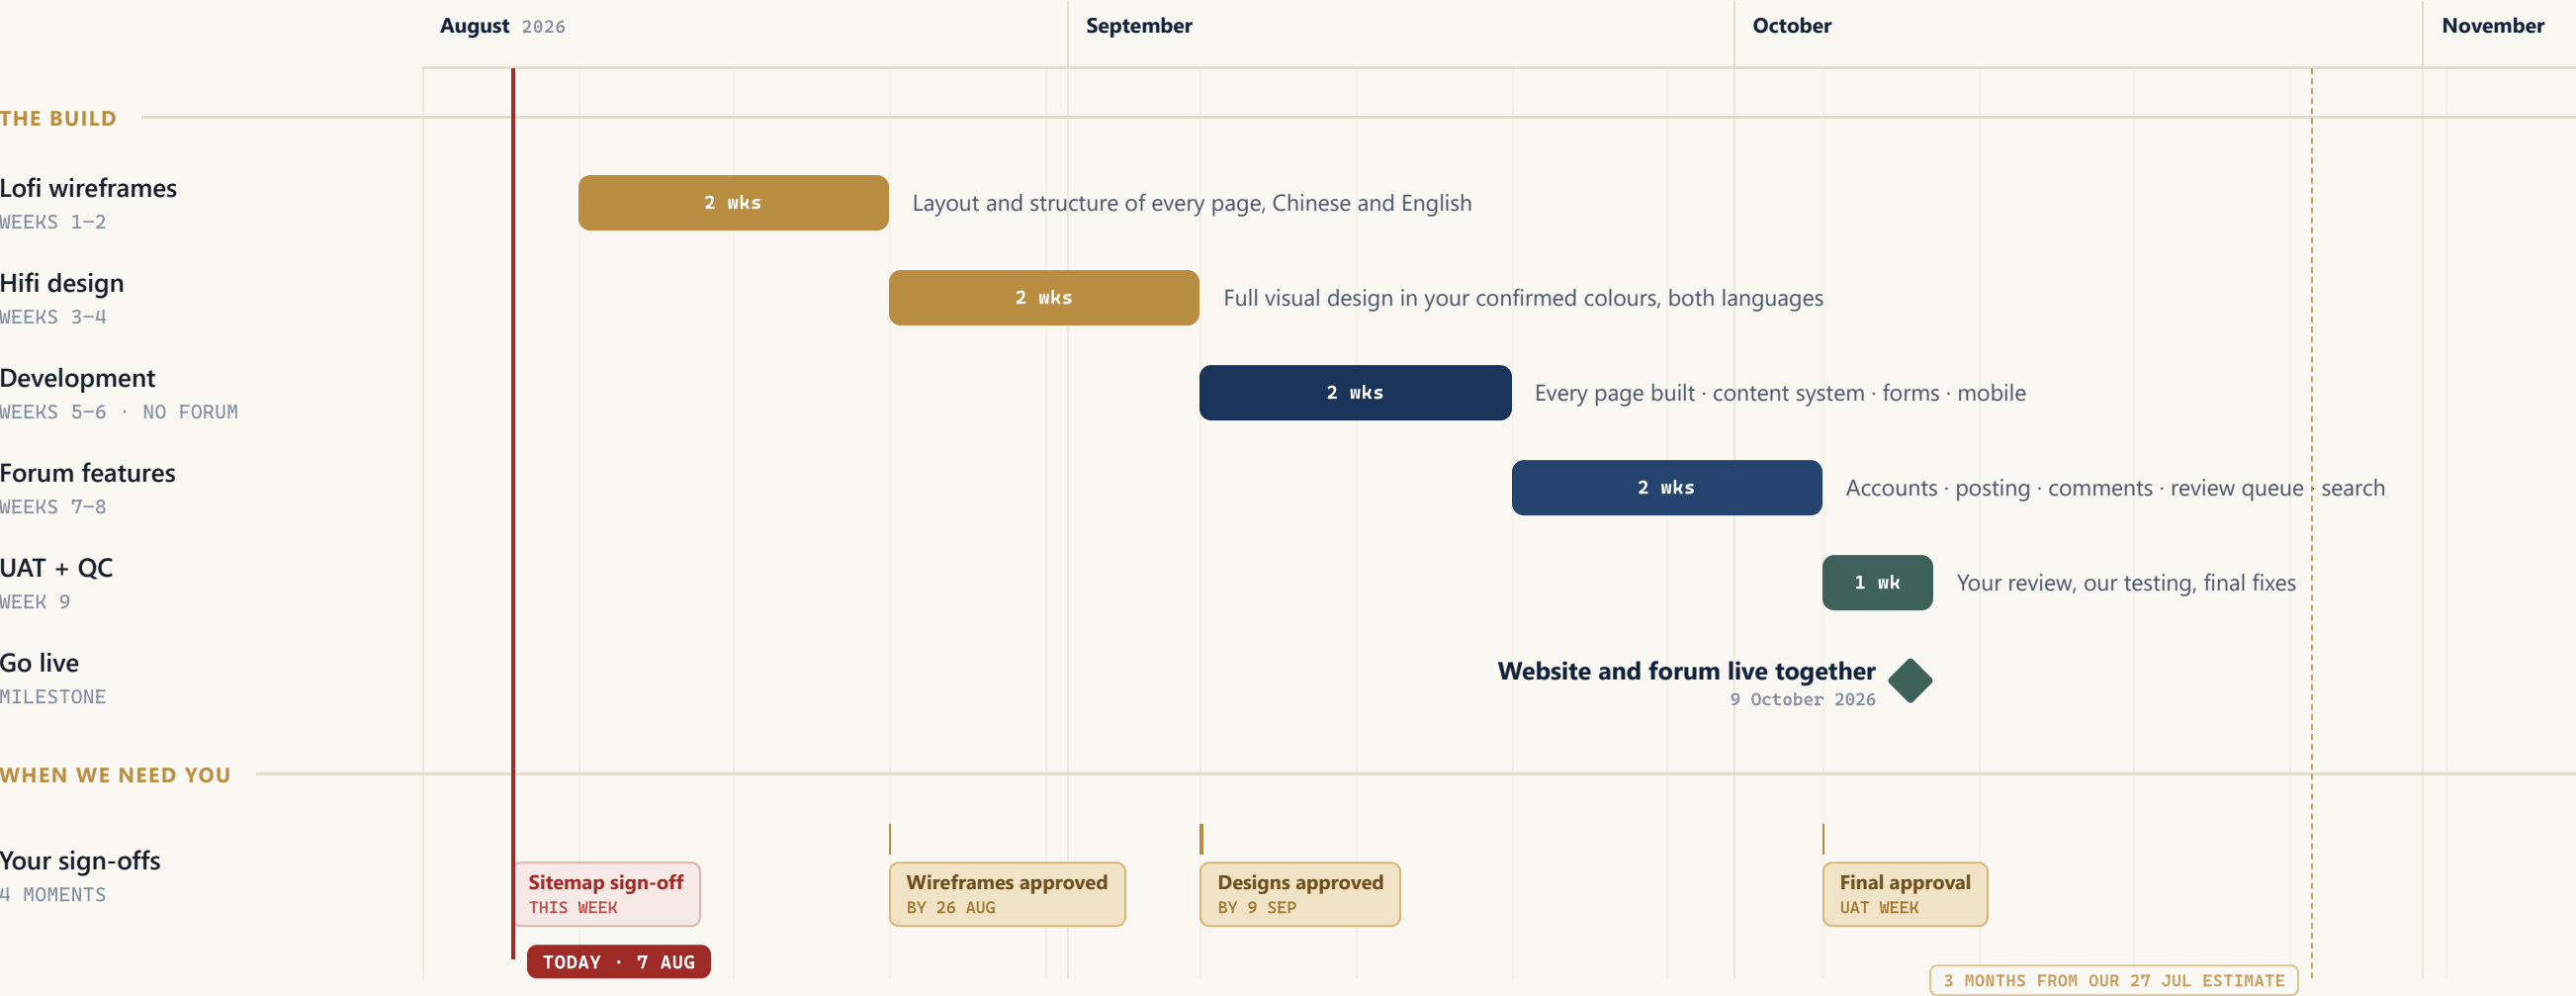

WHAT THIS TIMELINE ASSUMES

PLEASE READ

Two months covers the website **and** the forum, which is tighter than our original plan of building the forum after the demo. It is achievable, and these are the three things it depends on:

- Sign-offs inside three working days.** Each stage feeds the next, so a week spent waiting on approval is a week added to the end. The four points where we need you are marked on the timeline above.
- One round of feedback per stage.** We have allowed for one proper round of comments on the wireframes and one on the designs. A second round is completely fine — it simply moves the launch date, and we will tell you by how much on the day.
- The forum launches with the essentials.** Accounts, posting, comments, the review queue, search and 有用/举报 are all in. Extras such as image uploads, private messaging and following other members come after launch, once the forum has real members using it.

Some of the forum groundwork runs alongside the website build rather than after it, which is what makes the two months work — the website and the forum are one system, not two.

What you'll see, and when	STAGE BY STAGE	What we still need from you	TO PROTECT THE DATE	Already settled	NOTHING NEEDED
23 Aug	Wireframes — every page's layout, before any visual design	1 · Sitemap sign-off — this week.	Wireframes start on 10 August and this is the last thing holding them up.	Colour theme — confirmed on 4 August from your mockup, and already used across these documents.	
6 Sep	Full designs in your colours, Chinese and English	2 · Is the forum Chinese-only, or Chinese and English?	Your word list is Chinese-only, so if members can post in English we would need an English list too. Worth deciding before the forum work starts.	How posts get approved — your word list runs first and rejects the highest-risk terms instantly, an automated check reads the rest for context, and only the genuinely uncertain posts reach your reviewer. Nothing appears on the forum unchecked.	
20 Sep	A working website you can click through	3 · Who at CYS will review posts?	They will need to read Chinese. This is the one thing that can hold up the forum launch however well it is built.	Where the site lives — the Chinese site sits on its own address alongside your existing English site, which stays exactly as it is.	
4 Oct	The forum working end to end, including the review queue	4 · The remaining content — FAQ, terms and privacy.	The privacy page needs proper drafting because the forum collects members' information.		
9 Oct	Live				
